

UNIVERSITY OF HOUSTON
Campus Facilities Planning Committee
Agenda Item Description Form

1. **DATE:** March 1, 2016
2. **ITEM:** New Baseball Clubhouse
3. **REQUESTING DEPARTMENT:** Facilities, Planning and Construction
4. **CONTACT NAMES & PHONE NUMBERS:** Mei Chang (713)743-5729
Trent Williams (713) 743-5356
5. **PRESENTER:** Mei Chang
6. **RECOMMENDATION/
ACTION REQUESTED:** Approval of site and exterior product selection

- **SUMMARY:**

This project will provide for updated locker room and training facilities for the UH Baseball team. The project will be located between the existing tennis courts and the third base side of the baseball field.

- Present material samples
- Present updated rendering
- Present revised project schedule

7. **PROPOSED START DATE:** April 2016
8. **SUPPORTING DOCUMENTATION:** Renderings and physical samples


University of Houston Baseball Clubhouse

ID	Task Mode	Task Name	Duration	Start	Finish	Calendar Grid (Nov 29, Dec 20, Jan 10, Jan 31, Feb 21, Mar 13, Apr 3, Apr 24, May 15, Jun 5, Jun 26, Jul 17, Aug 7, Aug 28, Sep 18, Oct 9, Oct 30, Nov 20)																											
1		New Clubhouse Project Summary	253 days	Mon 12/14/15	Thu 12/1/16																												
2		Schematic Design	55 days	Mon 12/14/15	Fri 2/26/16																												
3		Design Development Drawings	14 days	Mon 2/29/16	Thu 3/17/16																												
4		Submit DD Drawings to U of H	0 days	Fri 3/18/16	Fri 3/18/16																												
5		U of H Review of DD Drawings	11 days	Mon 3/21/16	Mon 4/4/16																												
6		Submit 50% CD's to U of H	0 days	Fri 4/1/16	Fri 4/1/16																												
7		Pricing Review / Revision	12 days	Mon 4/4/16	Tue 4/19/16																												
8		Submit 100% CD's to U of H	0 days	Fri 4/15/16	Fri 4/15/16																												
9		U of H Review of CD's	15 days	Mon 4/18/16	Fri 5/6/16																												
10		Final Pricing	12 days	Mon 4/18/16	Tue 5/3/16																												
11		Start Construction - Clubhouse	0 days	Mon 5/9/16	Mon 5/9/16																												
12		Construction - Clubhouse	148 days	Mon 5/9/16	Wed 11/30/16																												
13		Construction Complete	0 days	Thu 12/1/16	Thu 12/1/16																												

Project: UH Baseball Clubhouse Date: Tue 4/5/16	Task		Project Summary		Manual Task		Start-only		Deadline	
	Split		Inactive Task		Duration-only		Finish-only		Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		External Tasks		Manual Progress	
	Summary		Inactive Summary		Manual Summary		External Milestone			

BELTWAY SOUTHWEST BUSINESS PARK

MAINTENANCE SUPPLY HEADQUARTERS - BRANCH OFFICE

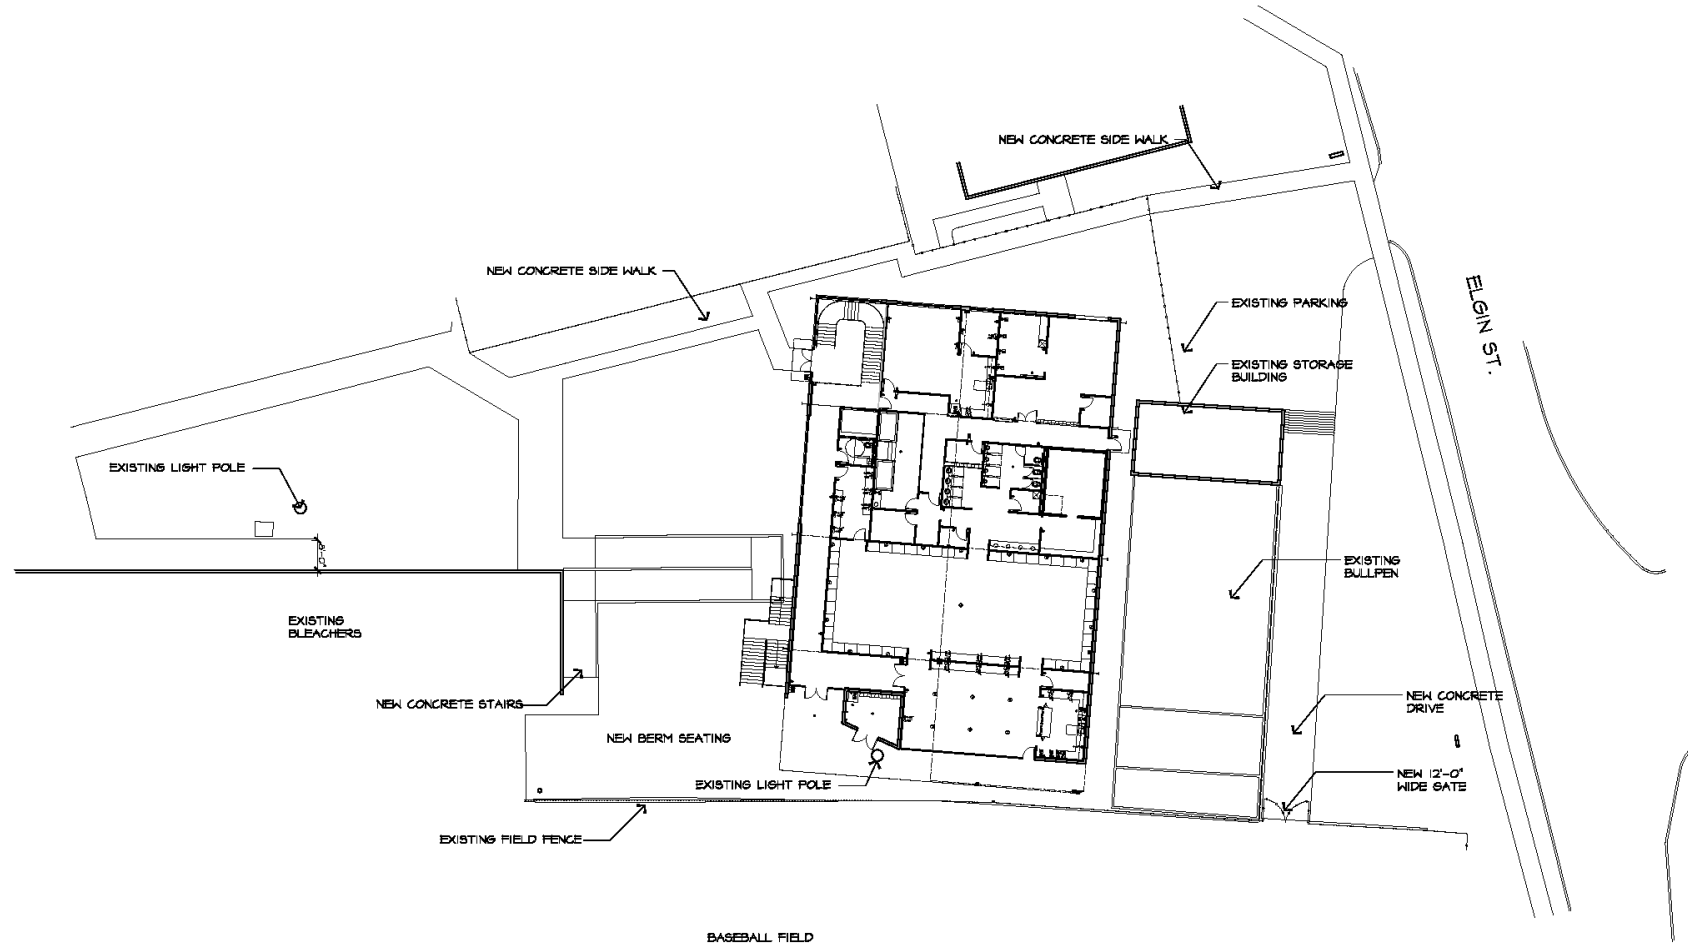

SCALE: 1/16" = 1'-0"



ARCHITECTS - PLUS www.architects-plus.com

INNOVATIVE CREATIVE

personal service

ARCHITECTURE DESIGN PLANNING INTERIORS

730 NORTH POST OAK DR., SUITE 311
HOUSTON, TEXAS 77024

PHONE 713.533.1370



UH
BASEBALL CLUBHOUSE



UH
BASEBALL CLUBHOUSE

2019 SINGLE GAME TICKETS NOW ON SALE
UH CIGARS CLUB

