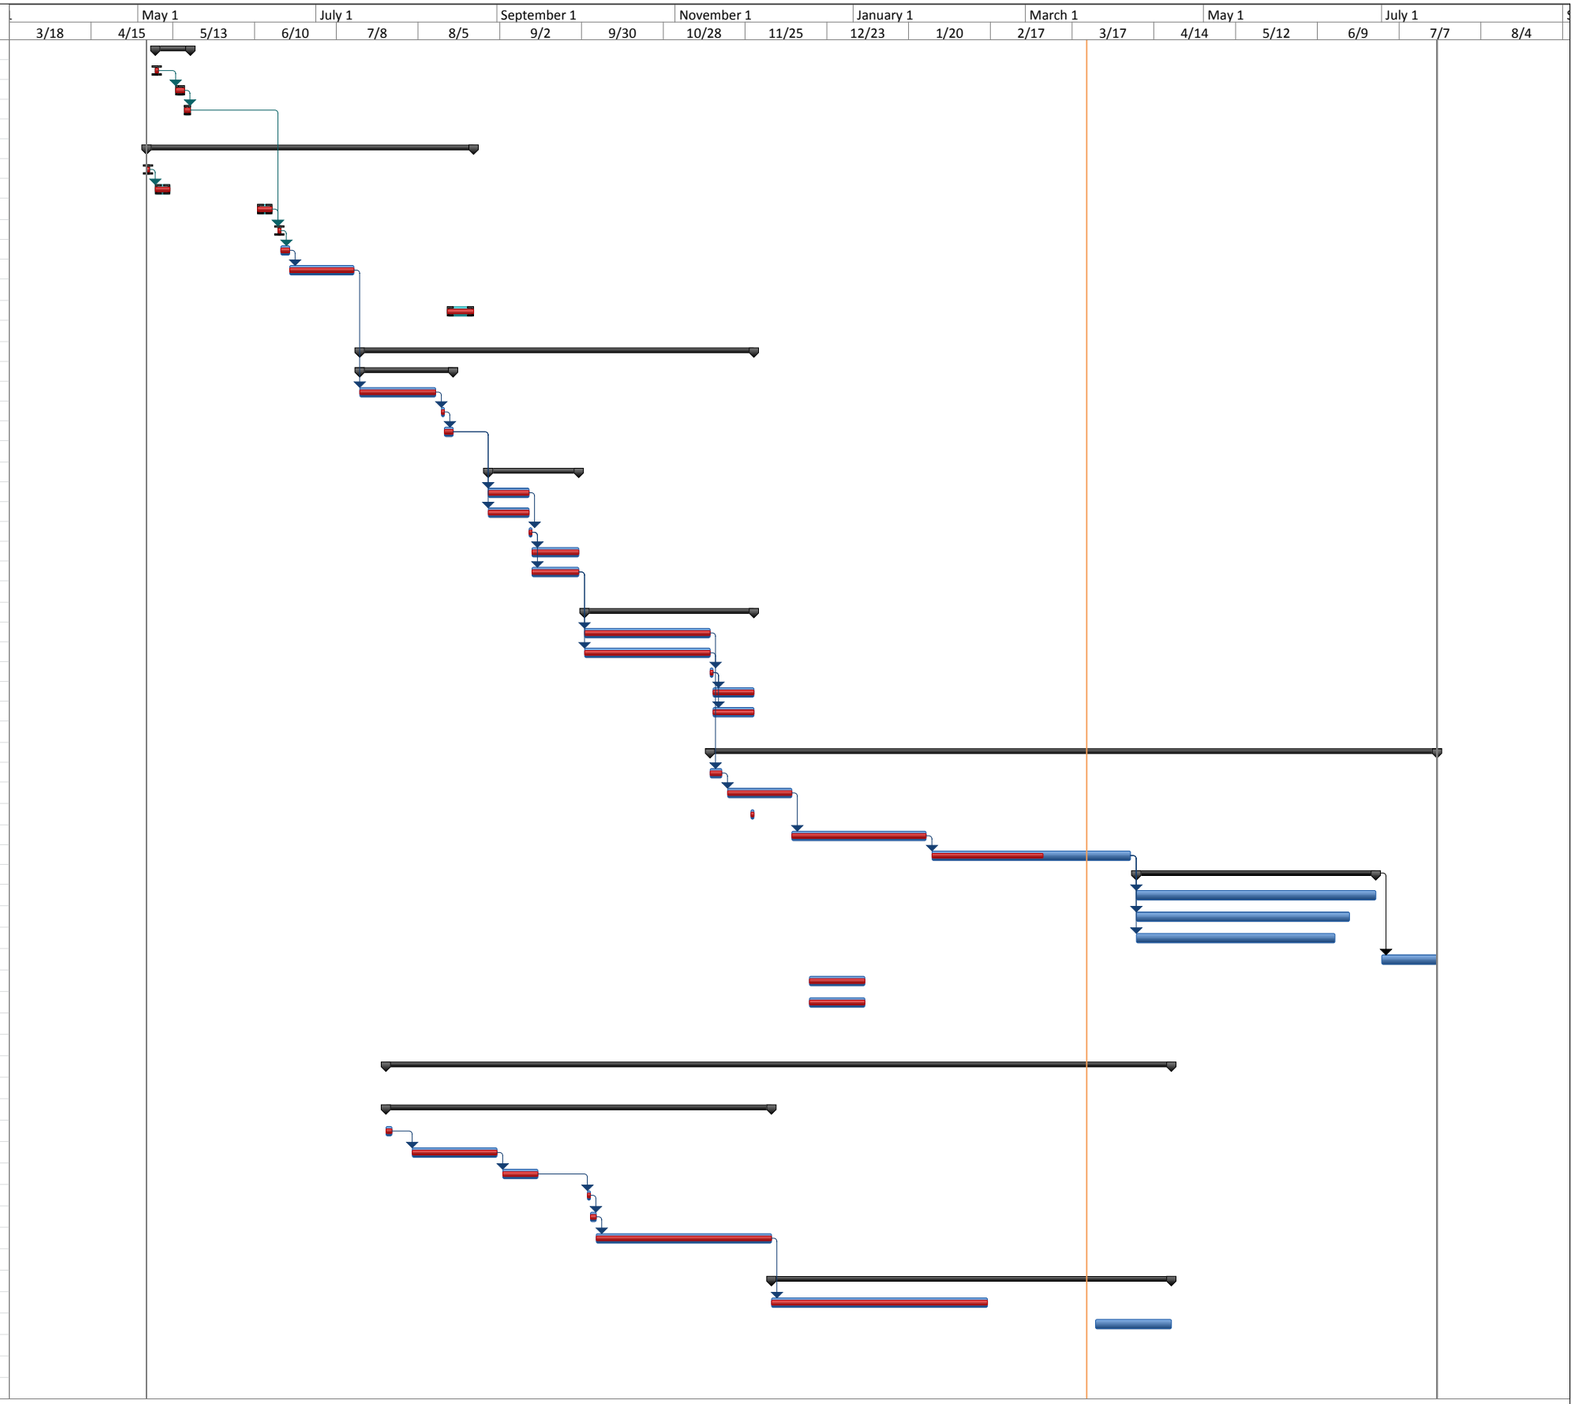ID		Task Name	Duration	Start	Finish	Predec	Task Mode	Resource Names
1	✓	**Project Setup**	**10 days**	**Mon 5/7/12**	**Fri 5/18/12**			
2	✓	Work Request Entered	1 day	Mon 5/7/12	Mon 5/7/12			
3	✓	PFA/PCB Submitted for Approval	3 days	Mon 5/14/12	Wed 5/16/12	2		
4	✓	Project Number Set Up	2 days	Thu 5/17/12	Fri 5/18/12	3		
5								
6	✓	**Pre-design - Scope Confirmation**	**80 days**	**Fri 5/4/12**	**Thu 8/23/12**			
7	✓	Kick-off Meeting and Visual Survey	1 day	Fri 5/4/12	Fri 5/4/12			
8	✓	URS to send UH proposal	5 days	Mon 5/7/12	Fri 5/11/12	7		
9	✓	URS to send revised proposal to UH	5 days	Mon 6/11/12	Fri 6/15/12			
10	✓	UH to send contract to URS	1 day	Mon 6/18/12	Mon 6/18/12	4,9		
11	✓	URS to return signed contract	3 days	Tue 6/19/12	Thu 6/21/12	10		
12	✓	UH to issue Executed Contract	16 days	Fri 6/22/12	Fri 7/13/12	11		
13								
14	✓	Rigging Inspection	7 days	Wed 8/15/12	Thu 8/23/12			
15								
16	✓	**Design and Documentation**	**97 days**	**Mon 7/16/12**	**Tue 11/27/12**			
17	✓	**50% Construction**	**24 days**	**Mon 7/16/12**	**Thu 8/16/12**			
18	✓	Drawings	20 days	Mon 7/16/12	Fri 8/10/12	12		
19	✓	Submit	1 day	Mon 8/13/12	Mon 8/13/12	18		
20	✓	UH Review	3 days	Tue 8/14/12	Thu 8/16/12	19		
21								
22	✓	**90% Construction**	**23 days**	**Wed 8/29/12**	**Fri 9/28/12**			
23	✓	Drawings	10 days	Wed 8/29/12	Tue 9/11/12	20		
24	✓	Specifications	10 days	Wed 8/29/12	Tue 9/11/12	20		
25	✓	Submit	1 day	Wed 9/12/12	Wed 9/12/12	23		
26	✓	UH Review	12 days	Thu 9/13/12	Fri 9/28/12	25		
27	✓	Fire Marshal Review	12 days	Thu 9/13/12	Fri 9/28/12	25		
28								
29	✓	**Bid Set**	**42 days**	**Mon 10/1/12**	**Tue 11/27/12**			
30	✓	Drawings	31 days	Mon 10/1/12	Mon 11/12/12	27		
31	✓	Specifications	31 days	Mon 10/1/12	Mon 11/12/12	27		
32	✓	Submit	1 day	Tue 11/13/12	Tue 11/13/12	31		
33	✓	UH Review	10 days	Wed 11/14/12	Tue 11/27/12	32		
34	✓	Fire Marshal Review	10 days	Wed 11/14/12	Tue 11/27/12	32		
35								
36		**Bidding and Construction**	**179 days**	**Tue 11/13/12**	**Fri 7/19/13**			
37	✓	Prepare RFP	4 days	Tue 11/13/12	Fri 11/16/12	30		
38	✓	Issue for bid	16 days	Mon 11/19/12	Mon 12/10/12	37		
39	✓	Pre-Proposal Conference	1 day	Tue 11/27/12	Tue 11/27/12			
40	✓	Contractor Selection	34 days	Tue 12/11/12	Fri 1/25/13	38		
41		Issue NTP	50 days	Mon 1/28/13	Fri 4/5/13	40		
42		**Construction (6/28/2012)**	**60 days**	**Mon 4/8/13**	**Fri 6/28/13**			
43		General Construction	60 days	Mon 4/8/13	Fri 6/28/13	41		
44		Access Control	53 days	Mon 4/8/13	Wed 6/19/13	41		
45		UH IT	50 days	Mon 4/8/13	Fri 6/14/13	41		
46		Punchlist	15 days	Mon 7/1/13	Fri 7/19/13	42		
47	✓	Costume Shop Relocation	15 days	Mon 12/17/12	Fri 1/4/13			
48	✓	Scene Shop Flooring Replacement	15 days	Mon 12/17/12	Fri 1/4/13			
49								
50								
51		**The Grove**	**193 days?**	**Wed 7/25/12**	**Fri 4/19/13**			
52								
53	✓	**Scope Verification**	**94 days**	**Wed 7/25/12**	**Mon 12/3/12**			
54	✓	RFQ Writing	2 days	Wed 7/25/12	Thu 7/26/12			
55	✓	Posting	21 days	Fri 8/3/12	Fri 8/31/12	54		
56	✓	Short List Selection	10 days	Mon 9/3/12	Fri 9/14/12	55		
57	✓	Interviews	1 day	Tue 10/2/12	Tue 10/2/12	56		
58	✓	Selection of Design Team	2 days	Wed 10/3/12	Thu 10/4/12	57		
59	✓	Contracting	42 days	Fri 10/5/12	Mon 12/3/12	58		
60								
61		**Design**	**99 days?**	**Tue 12/4/12**	**Fri 4/19/13**			
62	✓	Conceptual Design	54 days	Tue 12/4/12	Fri 2/15/13	59		
63		Design Change Order #01	20 days	Mon 3/25/13	Fri 4/19/13			
64		Construction Documents	TBD			62		
65								
66		**Bidding and Construction**	TBD			64
