Whaley New HRT Layout

Activity ID	Activity Name	OD	Start	Finish
Southeast Corridor		520	01-Oct-08 A	26-Oct-10
Construction Support Stage		185	11-Sep-09 A	28-Apr-10
SEG.2A - Wheeler / Scott to MLK - (STA 312+00 to...		185	11-Sep-09 A	28-Apr-10
Procurement		185	11-Sep-09 A	28-Apr-10
Procurement - Subcontract		185	11-Sep-09 A	28-Apr-10
Procurement - Permits		7	17-Mar-10	25-Mar-10
Stage 1		520	01-Oct-08 A	26-Oct-10
SEG.2A - Wheeler / Scott to MLK - (STA 312+00 to...		520	01-Oct-08 A	26-Oct-10
Design		175	20-Jul-09 A	31-Mar-10
Design - Civil		168	20-Jul-09 A	22-Mar-10
Design - Private Utilities		175	20-Jul-09 A	31-Mar-10
ROW		385	01-Oct-08 A	16-Apr-10
Utilities		156	18-Mar-10	26-Oct-10
SE-2A-FINPU-130	Segment 2A Public Utilitie...	10	23-Mar-10	06-Apr-10
SE-2A-STAPU-130	Start Milestone Public Utili...	0	07-Apr-10	
SE-2A-UH-130	U of Houston Utility Reloc...	60	07-Apr-10	16-Jul-10
Public Utilities		139	07-Apr-10	21-Oct-10
Private Utilities		156	18-Mar-10	26-Oct-10
Traction Power Substation		0	10-Aug-10	10-Aug-10
Signal Communication Buildings		0	10-Aug-10	10-Aug-10
Systems		0	21-Jan-10	21-Jan-10

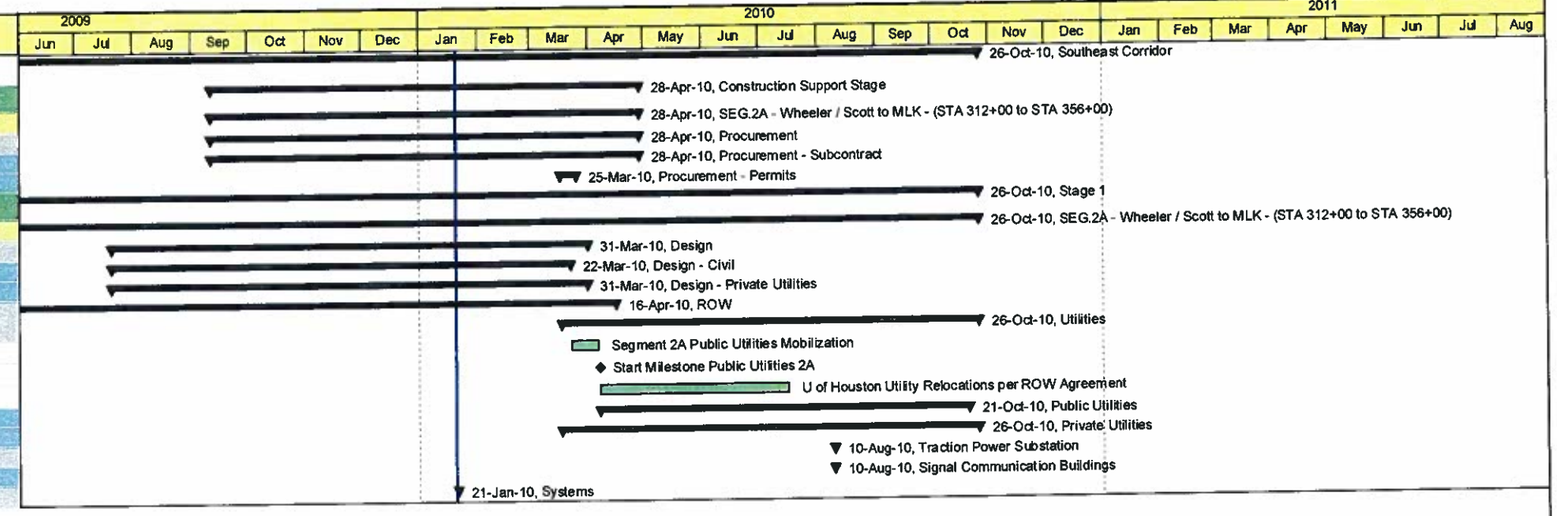

Actual Work | Critical Remaining Work | Su...
Remaining Work | Milestone

TASK filter: (Untitled Filter)_9.

© Primavera Systems, Inc.
