


8 Upgrade SA UHCL2

ID	ID	Task Name	% Complete	Start	Finish	Work	2nd Half						1st Half					
							May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr
0	0	PS8 Upgrade SAA UHCL	9%	1/3/2002	4/5/2005	31,299.05 hrs												
1	1	Convert UHCL Data Base	100%	1/3/2002	11/25/2002	1,182.4 hrs												
6	6	Work Plan Development	12%	9/26/2002	3/3/2003	80 hrs												
16	16	Establish Project Standards and Controls (update the Operation guide for PS 8)	0%	1/7/2003	1/31/2003	64 hrs												
17	17	Update & Test Modifications	9%	1/3/2002	10/31/2003	9,005.02 hrs												
383	383	Prepare System Test Plans	0%	5/3/2003	10/31/2003	476 hrs												
387	387	Develop Security	5%	5/5/2003	10/22/2003	322 hrs												
393	393	PS8 Infrastructure	33%	9/25/2002	1/15/2004	0 hrs												
394	394	PS8 Upgrade HR SA DatabasesV3	17%	5/1/2002	4/3/2004	7,122.82 hrs												
395	395	FREEZE Requirements	0%	11/3/2003	11/3/2003	0 hrs												
396	396	User Training	0%	11/3/2003	4/1/2004	1,018 hrs												
405	405	System Testing	0%	11/3/2003	1/30/2004	2,580 hrs												
412	412	System Test Go/No Go Decision	0%	1/30/2004	1/30/2004	0 hrs												
413	413	FREEZE UHS PeopleTools Development	0%	1/30/2004	1/30/2004	0 hrs												
414	414	User Acceptance Test	0%	2/2/2004	2/20/2004	1,060 hrs												
421	421	Acceptance Test Go/No Go Decision	0%	2/20/2004	2/20/2004	0 hrs												
422	422	Cutover & Verify Production System	0%	3/30/2004	4/4/2004	200 hrs												
430	430	Production Go/No Go Decision	0%	4/4/2004	4/4/2004	0 hrs												
431	431	Go Live	0%	4/5/2004	4/5/2004	0 hrs												
432	432	Post Go Live Implementation and Support	0%	4/5/2004	4/5/2005	8,188.8 hrs												

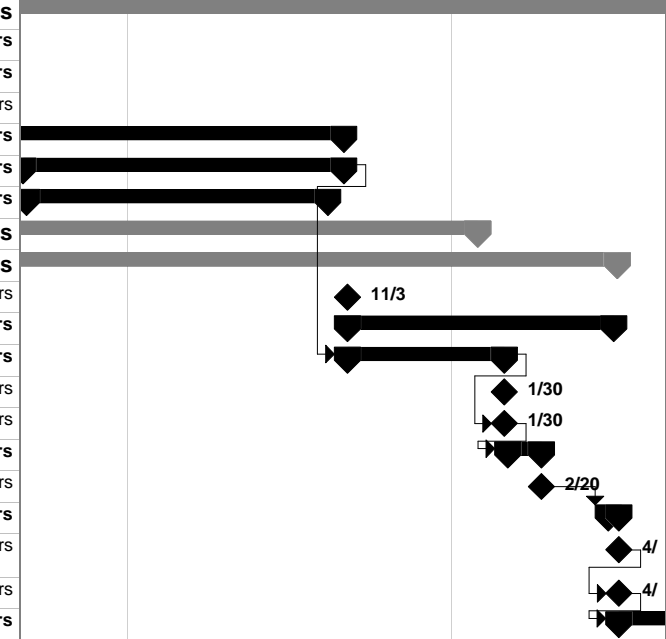

Project: PS8 Upgrade SAA UHCL
Date: 5/20/2003

Task		Milestone		External Tasks		External Milestone	
Split		Summary		External Milestone		Deadline	
Progress		Project Summary		External Milestone			
